
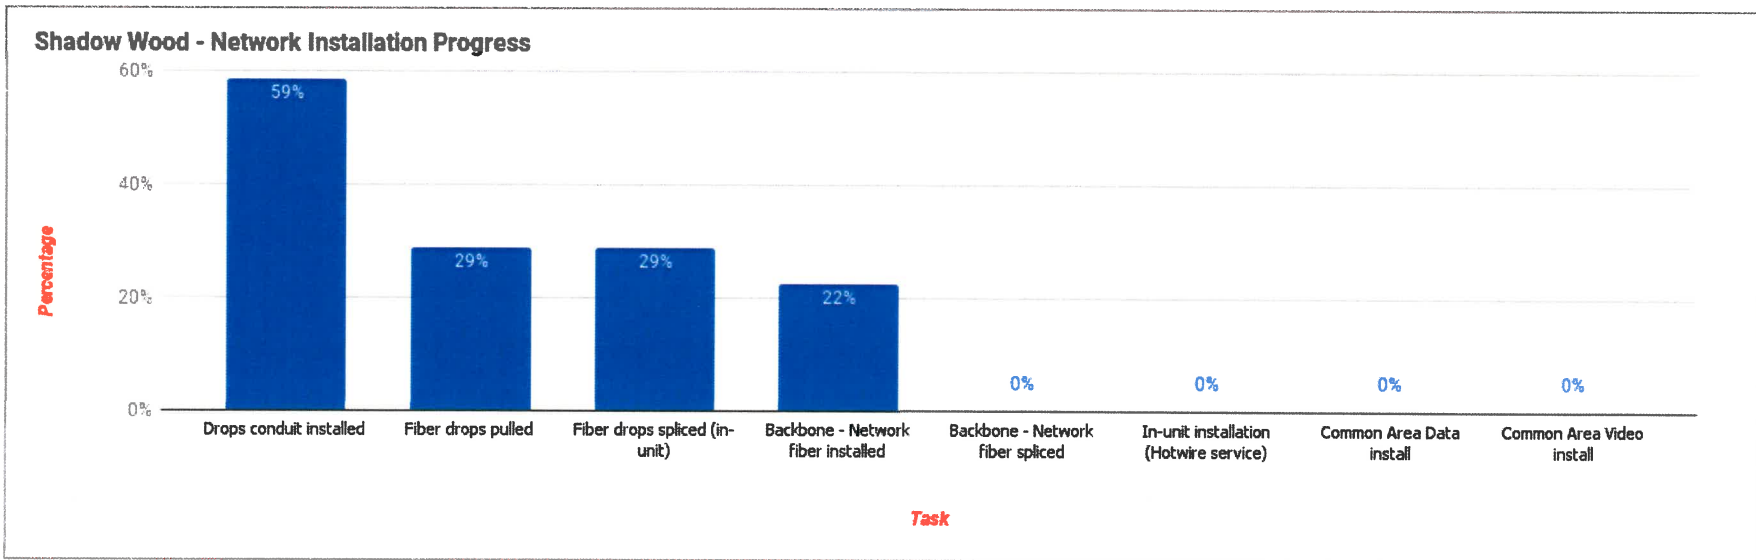


Shadow Wood - Weekly Update Summary

Wednesday, December 6, 2017

Task	Phase 1	Phase 2	Phase 3	Phase 4	Phase 5	Phase 6	Phase 7	Phase 8	Overall Progress
Drops conduit installed	100%	100%	100%	0%	0%	100%	0%	69%	59%
Fiber drops pulled	9%	100%	42%	0%	80%	0%	0%	0%	29%
Fiber drops spliced (in-unit)	9%	100%	42%	0%	80%	0%	0%	0%	29%
Backbone - Network fiber installed	69%	100%	0%	0%	0%	10%	0%	0%	22%
Backbone - Network fiber spliced	0%	0%	0%	0%	0%	0%	0%	0%	0%
In-unit installation (Hotwire service)	0%	0%	0%	0%	0%	0%	0%	0%	0%
Common Area Data install	0%	0%	0%	0%	0%	0%	0%	0%	0%
Common Area Video install	0%	0%	0%	0%	0%	0%	0%	0%	0%

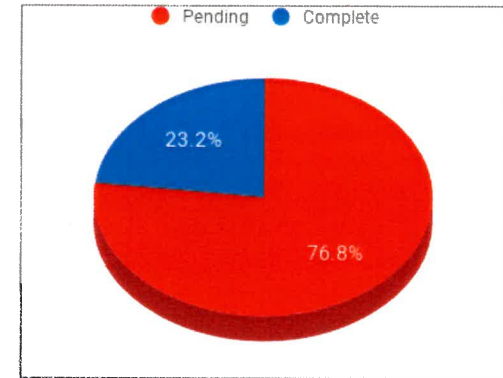

Highlights:

- * Hotwire had two minor escalations last week
- * Next week Pete from Hotwire will be working with the structural engineer to resolve the roof tile issue
- * Morningside condo installation started
- * 5% increase in production from the previous week

Shadow Wood - Network Installation Progress

