
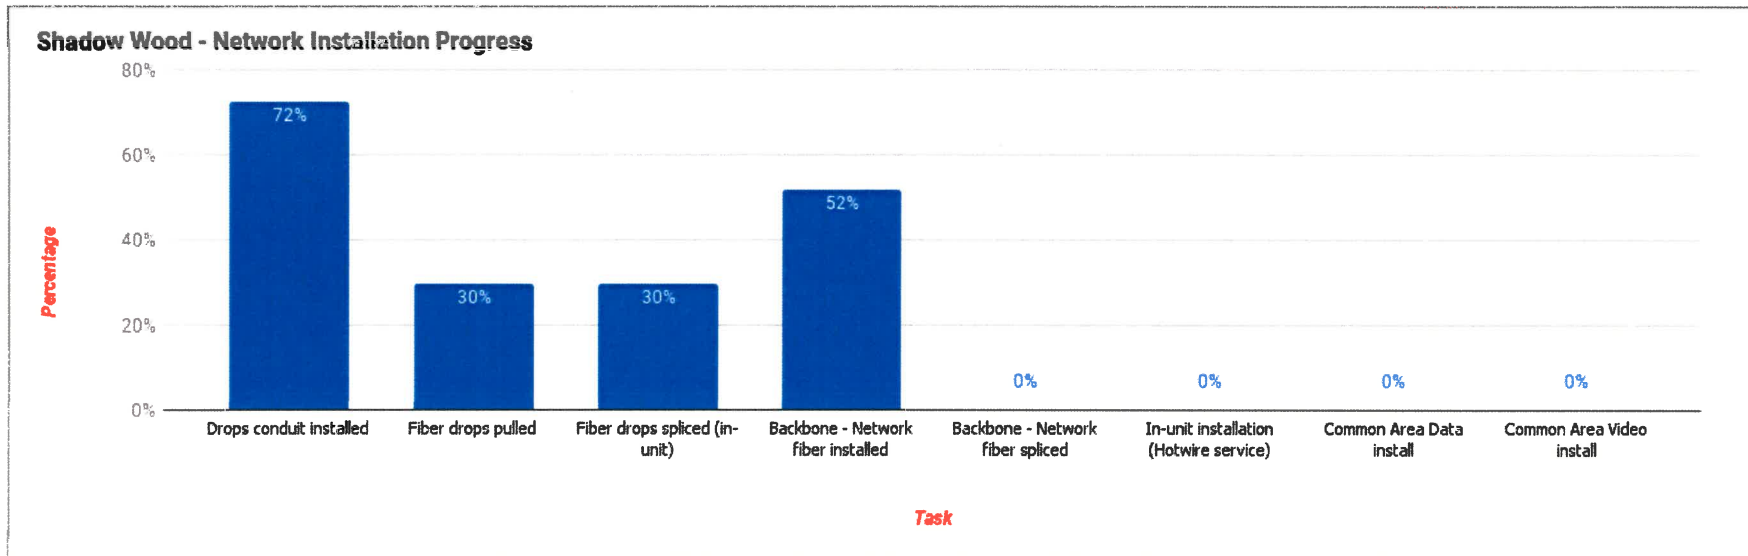


Shadow Wood - Weekly Update Summary

Monday, December 25, 2017

Task	Phase 1	Phase 2	Phase 3	Phase 4	Phase 5	Phase 6	Phase 7	Phase 8	Overall Progress
Drops conduit installed	93%	100%	100%	0%	80%	100%	0%	100%	72%
Fiber drops pulled	43%	100%	42%	0%	80%	0%	0%	0%	30%
Fiber drops spliced (in-unit)	43%	100%	42%	0%	80%	0%	0%	0%	30%
Backbone - Network fiber installed	100%	100%	45%	0%	0%	88%	0%	30%	52%
Backbone - Network fiber spliced	0%	0%	0%	0%	0%	0%	0%	0%	0%
In-unit installation (Hotwire service)	0%	0%	0%	0%	0%	0%	0%	0%	0%
Common Area Data install	0%	0%	0%	0%	0%	0%	0%	0%	0%
Common Area Video install	0%	0%	0%	0%	0%	0%	0%	0%	0%

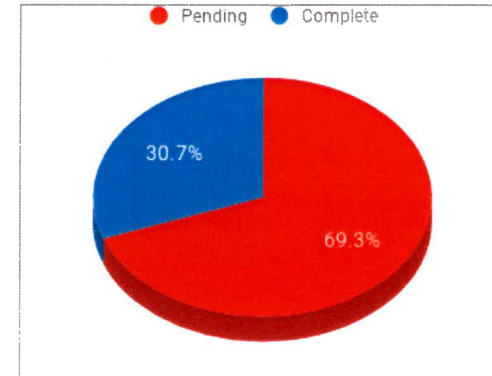

Highlights:

- * 4.6% increase in production from the previous week
- * Four total escalations
- * There are few buildings in Morningside with no access until 2018
- * Headend construction is going well and on target

Shadow Wood - Network Installation Progress

